


## POINT 1 - Status

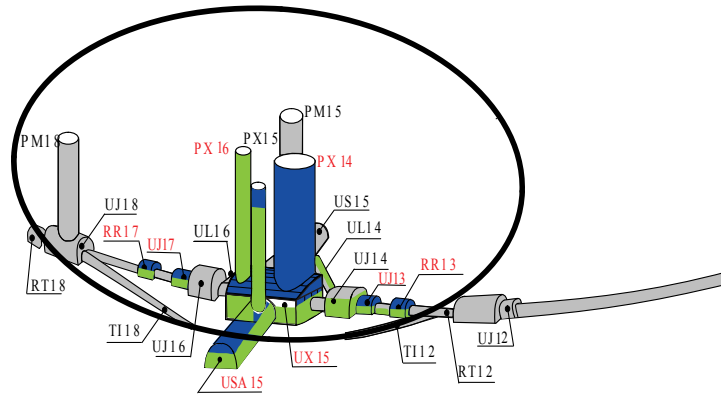

- Existing Structures
- LHC Project Structures
- LHC Excavated Structures
- LHC Completed Structures (CE)
- LHC Completed Structures (CV, EL, HM, MA)

IN PROGRESS	%	FINISH DATE	FUTURE WORKS	START DATE	FINISH DATE
<u>UX 15 Equipment</u> EL CV HM MA		Under Way			
<u>US 15 Equipment</u> EL CV HM MA		Under Way			
<u>US 15 Repair Works</u>	10	26 Sep. 2003			
<u>Prefabricated Beams</u> Top of PX 14 - 15 Shaft	20	17 Oct. 2003			
