


## TI2 Area - Status

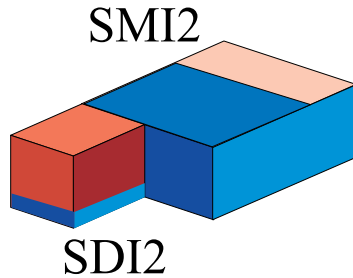

- Existing Buildings
- LHC Project Buildings
- LHC Completed Buildings (CE)
- LHC Completed Buildings (CV, EL, HM, MA)

IN PROGRESS	%	FINISH DATE	FUTURE WORKS	START DATE	FINISH DATE
<u>SMI2</u>		31.01.03			
Gantry crane support beams	100				
Roof	100				
Cladding	80				
Aerochauffeur units	90				
Floor slab	100				
<u>SDI2</u>					
Floor slab	25	31.01.03			
