


## POINT 1- Status

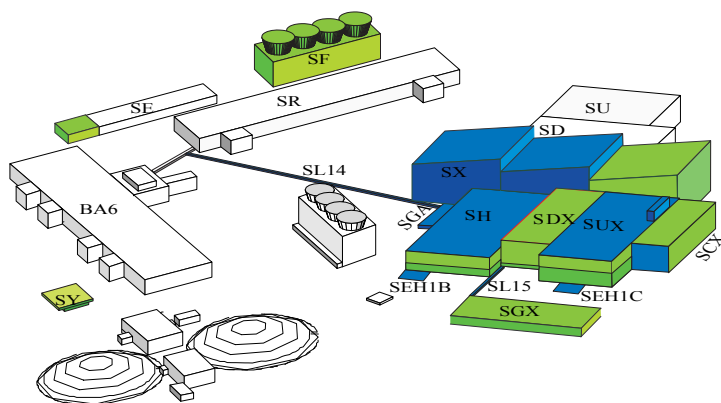

- Existing Buildings
- LHC Project Buildings
- LHC Completed Buildings (CE)
- LHC Completed Buildings (CV, EL, HM, MA)

IN PROGRESS	%	FINISH DATE	FUTURE WORKS	START DATE	FINISH DATE
<u>SDX1</u> : HM (door)	100				
<u>SX1</u> : Finishing works + doors (HM)	90	30 Oct. 2003			
<u>SE1</u> : Extension	50	26 Sep. 2003			
Roads and Car Park finishes	50	26 Sep. 2003			
All buildings HM CV EL MA		Under Way			
